

Headquarters, Department of the Army



Fort Monmouth, NJ

Conveyance Progress Report as of 1 April 2015



Office of the Assistant Chief of Staff for Installation Management (OACSIM)
Operations Directorate– Base Realignment and Closure (ODB)

TABLE OF CONTENTS

Summary	2
Environment	3
Reuse Plan	4
Programmatic Agreement	5
Conveyance Plan	6-7
Key Milestones Achieved	8



Front entrance to Fort Monmouth, New Jersey.

BRAC 2005 Recommendation

The 2005 Base Closure and Realignment Commission recommended the closure of Fort Monmouth. Major realignments included consolidation and movement of Team Command, Control, Communications, Computers, Intelligence, Surveillance and Reconnaissance (C4ISR) to Aberdeen Proving Ground, MD (APG), relocation of United States Military Academy Prep School (USMAPS) to West Point, NY, and consolidation of the Program Executive Office Enterprise Information Systems (PEO EIS) mission at Fort Belvoir, VA. The actions were completed and the installation was closed on 12 September 2011.

History

Fort Monmouth was established in 1917. The original name of Fort Monmouth was Camp Little Silver in 1917, then renamed Camp Alfred Vail. The Fort was originally established as a temporary facility for training the 1st and 2nd Reserve Signal Battalions, in anticipation of the United States' involvement in World War I. The Chief Signal Officer authorized the purchase of Camp Alfred Vail in 1919 when the Signal Corps School relocated to Camp Vail from Fort Leavenworth that year. In 1925, the installation was granted permanent status and renamed Fort Monmouth. Over the years, Fort Monmouth became one of the Army's major research and development centers for high-tech systems.

Prior to its closure under BRAC 2005, Fort Monmouth had been realigned under three earlier BRAC rounds. The 1988 BRAC Commission directed that the Army relocate Information Systems Command (ISC) from Fort Monmouth to Fort Devens, MA. The 1991 BRAC Commission directed the move of the Electronic Technology Device Laboratory from Fort Monmouth to Adelphi, MD. The 1993 BRAC Commission directed the relocation of the Chaplain School to Fort Jackson, SC and the movement of the U.S. Army Communication-Electronics Command's Headquarters out of the leased space and into space at Fort Monmouth vacated by the 513th Military Intelligence Brigade (a non-BRAC movement) and the Chaplain School. It also directed the disposal of excess facilities and real property at Evans and Charles Woods subposts. On 20 November 2013, the final parcel from the BRAC 1993 realignment of Fort Monmouth was conveyed. With this conveyance, the Army completed 100% conveyance (220 acres) of all BRAC 93 excess property.

Current Status

The Army and the Fort Monmouth Economic Revitalization Authority (FMERA) signed the Memorandum of Agreement (MOA) for Economic Development Conveyance (EDC) of Phase I Parcels on 25 June 2012. Phase I consisted of 556 acres. The first property transfer (Parcel E—55 acres) occurred on 27 June 2012. The second property transfer (Paterson Army Health Clinic Parcel—16 acres) occurred on 17 September 2013. The bulk of the Phase I property transferred on 29 May 2014 with the exception of the marina, Megill Housing and environmental cut-outs. Megill Housing transferred on 16 December 2014. Representatives from FMERA, DASA IE&E, OGC, and ACSIM BRAC-D met on 6 March 2014 and agreed to a "lump-sum buyout" agreement for the Phase II Parcels (remainder of Main Post property—570 acres). Phase II is scheduled to convey to FMERA under a less than fair market EDC. The FOST is in development and anticipate it being final in June 2015.

Property Description

Fort Monmouth, NJ (1,126 acres) contains two areas, the Main Post and Charles Wood. The main post includes R&D facilities, office space, housing, retail areas, and a marina. The Charles Wood area includes R&D facilities, office space, housing, a golf course and a firing range.

Caretaking Status

A staff of two Federal employees remain on Fort Monmouth to provide caretaker services. These services include oversight of facilities maintenance and operation, property accountability, local interface with community leaders, and on-the-ground coordination of the environmental clean-up and property conveyance efforts.




Main Post family housing.

Fort Monmouth Environmental Clean-up

Fort Monmouth is a relatively clean Post since its primary mission was Research and Development. The Army has identified the traditional contamination sites on this property, e.g., petroleum, volatile chemicals, underground and above ground storage tanks, toxic chemicals, hazardous wastes, etc. After extensive analysis, the Army determined that the risk to health and the environment from these items is minimal and can be addressed with Land Use controls. The Army continues to work closely with the FMERA and the New Jersey Department of Environmental Protection (NJDEP) to resolve remaining environmental issues. Given the age of the installation, both lead based paint and asbestos are present, quantified and will be dealt with in accordance with regulatory requirements. There appear to be no environmental impediments to the transfer of the property although there may be some “carve outs” to allow most parcels to transfer until remediation efforts can be completed.

Fort Monmouth, Reuse Plan

Fort Monmouth is contained within three municipalities, the Boroughs of Tinton Falls, Eatontown, and Oceanport; and is located adjacent to the Boroughs of Shrewsbury and Little Silver. The plan was prepared by a multi-disciplinary team including planners, landscape architects, architects, environmental scientists and engineers, economic analysts, cultural resource specialists, and transportation planners and engineers. Various advisory committees, representatives from Monmouth County and the Municipalities, and members of the State of New Jersey Interagency Team provided input into the plan. FMERA has the authority to adjust the plan as necessary to accommodate purchasers; however, the basic land use should stay consistent within the plan.

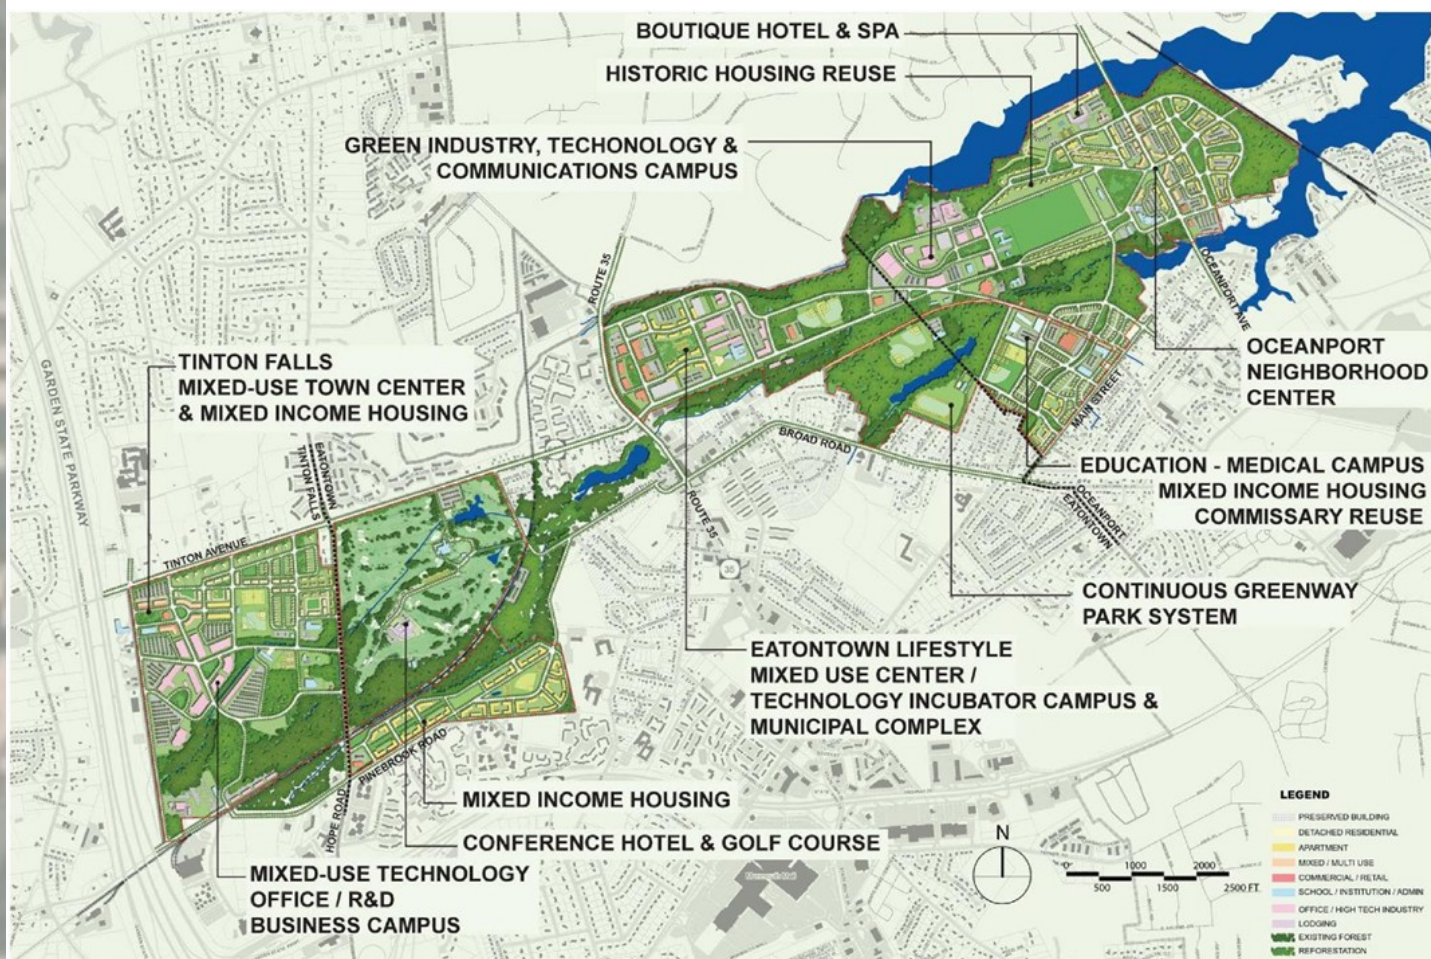

20 Year Vision for Redevelopment of Fort Monmouth Properties

Fort Monmouth, Programmatic Agreement, Section 106

The buildings within Fort Monmouth display a wide range of design characteristics and uses. These buildings were developed over time in different architectural styles in response to the needs of the garrison and mission. Based upon the buildings' architectural merit, their association with significant events in American history such as World War II and the Cold War, there are nearly 100 buildings eligible for the State and National Register of Historic Places.

With the pending closure of Fort Monmouth, the Army and the New Jersey State Historic Preservation Office signed a Programmatic Agreement in October 2009. As a part of this agreement, FMERA acting on behalf of the Army, is required to participate in the Section 106 review process and consult with the State Historic Preservation Office prior to implementing projects that impact historic properties.

The New Jersey State Historic Preservation Office determined that three historic districts within Fort Monmouth are eligible for listing on the National Register of Historic Places. The largest of the districts is the Fort Monmouth Historic District (main post) which includes the parade ground (and associated World War II Memorial), family housing, offices, and fire station. The other two historic districts include the Charles Wood Historic District and the Charles Wood Residential Historic District. The focal point of the Camp Charles Wood Historic district is Gibbs Hall, a 1926 Tudor Revival style golf clubhouse as well as the surrounding golf course.



World War II barracks and training facilities in the background with visiting quarters in the foreground.


Fort Monmouth Property Conveyance Plan

All parcels at Monmouth are being transferred under a less than market value EDC to FMERA. The conveyance plan includes two phases.

Phase I. Consisted of 556.2 acres as illustrated in the tables below. Most Charles Wood property, plus Parcel B (Main Post), transferred on 29 May 2014. Megill Housing transferred on 16 December 2014. The Marina Parcel, minus environmental carve-outs, is scheduled for transfer by September 2015.


Phase II. Phase II is the remainder of the Main Post property—569.8 acres. Representatives from FMERA, DASA IE&E, OGC, and ACSIM BRAC-D met on 6 March 2014 and agreed to a “lump sum buyout” agreement for the Phase II EDC property. Phase II, minus environmental carve-outs, is tentatively scheduled for transfer by August 2015.

Property Conveyed (548 of 1,126 total acres) and Projected:

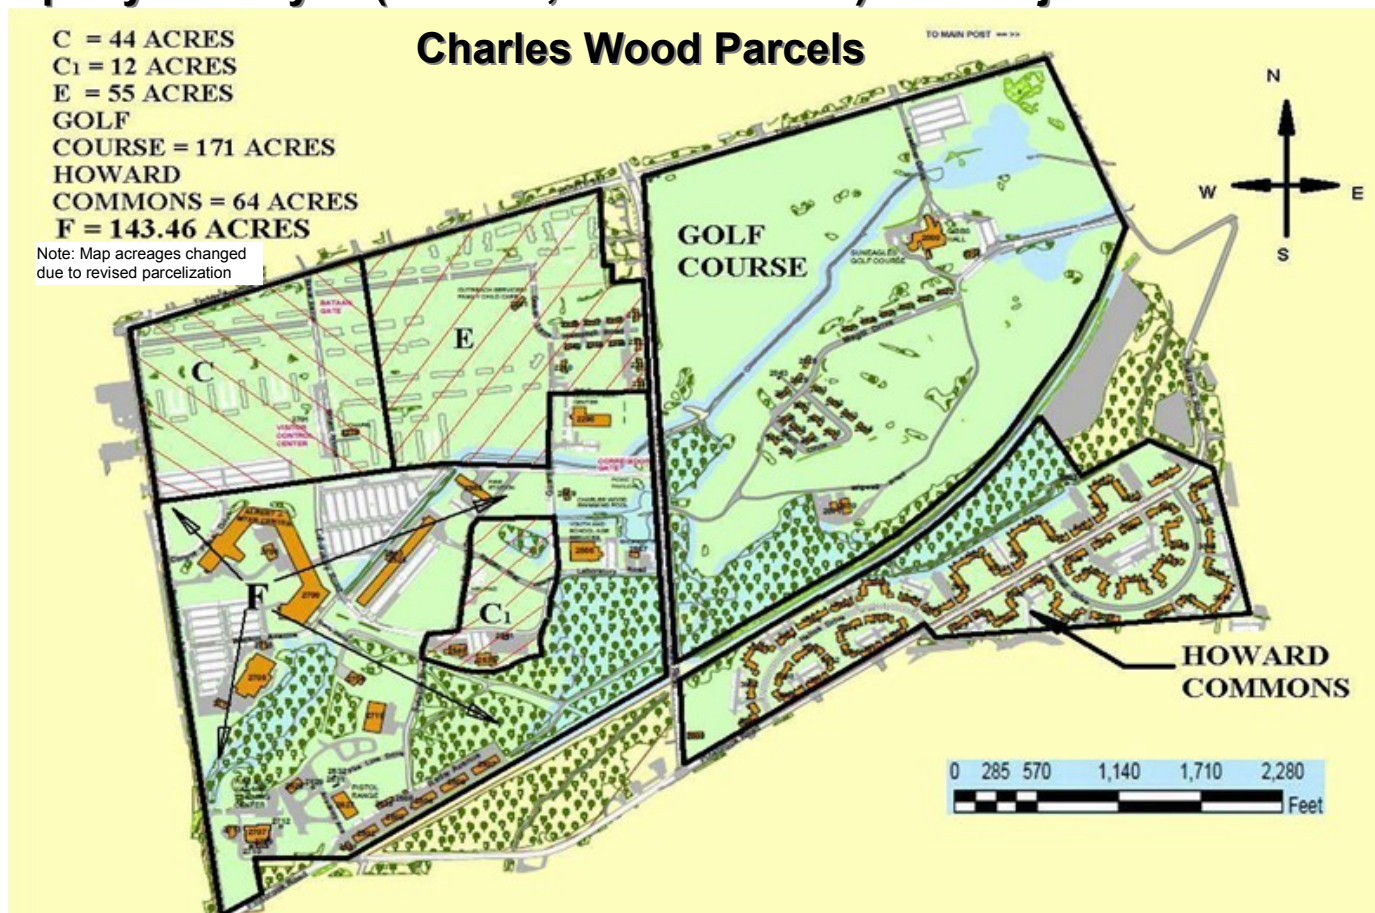

Parcel Name	Parcel Acres	Disposal Date	Parcel Recipient	Conveyance Authority
Phase I, Parcel E	55.0	27 Jun 2012	FMERA	EDC
Phase I, Golf Course (Minus Megill Housing)	161.0	29 May 2014	FMERA	EDC
Phase I, Parcel C & C ₁	63.9	29 May 2014	FMERA	EDC
Phase I, Howard Commons	64.0	29 May 2014	FMERA	EDC
Phase I, Parcel F	122.8	29 May 2014	FMERA	EDC

As of 1 April 2015

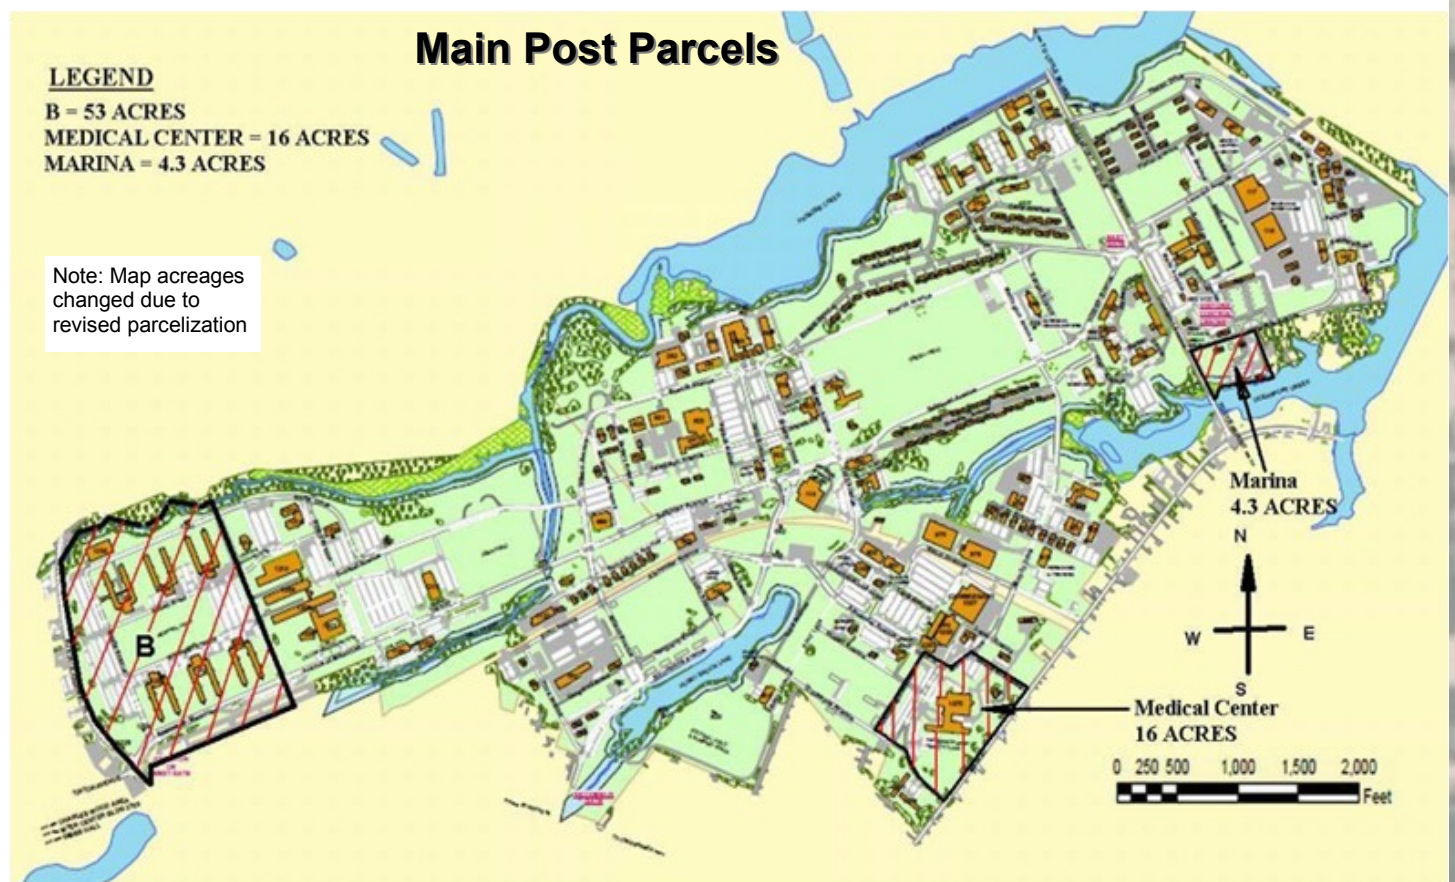

Parcel Name	Parcel Acres	Disposal Date	Parcel Recipient	Conveyance Authority
Phase I, Clinic Parcel	15.5	17 Sep 2013	FMERA	EDC
Phase I, Parcel B	55.4	29 May 2014	FMERA	EDC
Phase I, Megill Housing	10.0	16 Dec 2014	FMERA	EDC
Phase I, Marina	4.8	4th Qtr FY 15	FMERA	EDC
Phase I, Parcel F (Env)	3.9	3rd Qtr FY16	FMERA	EDC
Phase II, Main Post	540.0	4th Qtr FY15	FMERA	EDC
Phase II Main Post (Env)	29.8	4th Qtr FY16	FMERA	EDC

As of 1 April 2015



Megill Circle housing in Camp Charles Wood Residential Historic District. A Residential Historic District located in the center of the golf course that includes a total of 21 duplexes (42 units) constructed circa 1949 to 1955. Army licensed this housing to FEMA to house Hurricane Sandy victims and FEMA paid to renovate the quarters.

Key Milestones Achieved

- The Army and FMERA signed the Memorandum of Agreement (MOA) for Economic Development Conveyance of Phase I Parcels on 25 June 2012.
- The Army transferred the first parcel (Parcel E—55 acres) to FMERA on 27 June 2012.
- FMERA closed (deeded) Parcel E to CommVault on 29 January 2013.
- The Army transferred the Clinic Parcel (16 acres) to FMERA on 17 September 2013.
- FMERA Board closed (deeded) the Clinic Parcel to Acute Care on 19 March 2014.
- Army and FMERA met March 6, 2014 and agreed to a “lump-sum buyout” agreement for the Phase 2 Parcels, which includes the remainder of the Main Post property.
- Army and FMERA signed the EDC Phase 2 deal points on 13 June 2014.
- FMERA forwarded their EDC application for Phase II on 25 August 2014.
- The Army transferred Megill Housing (10 acres) to FMERA on 17 December 2014.

Significant Event

- Hurricane Sandy struck New Jersey on 30 October 2012. Parts of Fort Monmouth were under 2-3 feet of water and there were some buildings on Main Post that had basement flooding. In comparison to more coastal areas, Fort Monmouth bore the brunt of the storm relatively well. The Federal Emergency Management Agency (FEMA) requested Fort Monmouth provide emergency housing for displaced families. USACE licensed the Fort Monmouth Lodging Complex (eight buildings; 270, 271, 360, 361, 362, 363, 364, and 365), and Megill Housing to FEMA for up to 18 months (through 25 May 2014). USACE renovated Bldg 365 (45 units), Bldg 360 (28 units) and Megill Housing (21 duplexes/42 units). This is a total of 115 units to house displaced families. Displaced families originally occupied all 115 units but as units became vacant, FEMA did not reassign them. FEMA requested an extension for buildings 360/365 through 25 September 2014 but not the Megill Housing. FEMA moved the final five remaining displaced families to other FEMA housing in the local area and formally vacated Fort Monmouth housing on 2 September 2014.



World War II Memorial on main post parade ground.
